



Project No. 6334 - SW 91st St. Resurfacing and provide traffic calming measures

Design Details

Design Engineers- Kimley-Horn & Associates
 Design Cost- \$241,124.70
 (Combination of lump sum and not-to-exceed amount)
 Construction Contract Cost - \$1,494,935.62
 % Design Complete- 100%
 % Construction Complete - 0%

Project Schedule

100% Design— July 2010
 Award— February 2011
 NTP— June 2011
 Final Comp— November 2011


Project Description

- Resurfacing of SW 91st Street from Newberry Road to SW 8th Avenue.
- Widen and relocation of multi-use path
- Total length of project = approximately 1 mile.

Design Team

Design: Earl Wills, PE, KHA
 PM: Chris Zeigler, ACPW

Project Progress

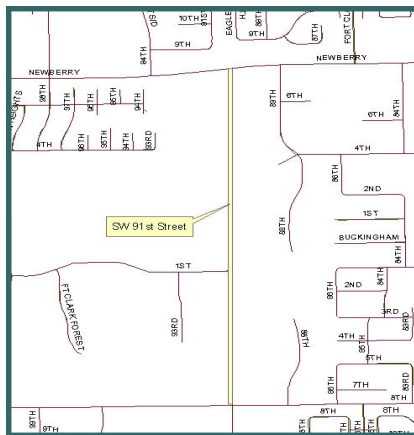

- **Utilities:** Utility pole relocation are required to meet clear zone requirements.
- **Drainage:** Kimley-Horn and Associates completed a drainage analysis and determined that the proposed modifications will not increase flooding.
- **Sidewalk:** The sidewalk will be resurfaced with ADA improvements. The plans have been revised to widen the sidewalk to 8' and relocate to the edge of the right-of-way wherever possible.
- **Public Involvement:**
 - A third public meeting was held on September 4, 2008 at 6:30pm.
 - Citizens' Advisory Committee presentation on October 1, 2008.
 - Scenic Road Committee meeting on October 14, 2008.
 - A fourth public meeting was held on November 21, 2008
 - Board of County Commissioners conceptually approved the 60% design plans on December 9, 2008.
 - Public Works presented the project to the Bicycle/Pedestrian Advisory Board on February 24, 2009.
 - Public Works staff presented the revised plans to the Board of County Commissioners (BOCC) on March 24, 2009.
 - BoCC approved 60% plans on August 25th
 - BoCC approved 90% plans on February 23, 2010.
- **Construction:**
 - Bid opened on December 15, 2010
 - Lowest apparent bidder was DAB Constructors at \$1.4 million.
 - BoCC awarded bid to DAB Constructors on February 8, 2011.
 - BoCC approved construction contract on April 12, 2011
 - Contract time is 150 days.
 - Contract time began on June 13, 2011.
 - The contractor has completed all the milling and initial layer of asphalt, curb and gutter, driveways and the asphalt path. The project is over 50% complete.
 - The contractor continues to work on grading and installing the landscaping and reinstalling the fence.
 - Preparing a change order to add additional time to the contract due to utility conflicts
